

	(1)	Name	Duration	Start	Finish	Predecessors	Resources	Ap	r 6 - A	\pr 12	? '1 5
	•	Ivalile	Duration	Start	Fillion	Fredecessors	Resources	M	Т	W	Т
1		☐ Proyecto TMN Integral	152d?	16/04/2015	13/11/2015						
2		□Analisis	37d	16/04/2015	05/06/2015						
3		☐ Analsis y Reelevamiento de Procesos	2d	16/04/2015	17/04/2015						
4	□	Configuration Manager	2d	16/04/2015	17/04/2015						
5	1	Inventory	2d	16/04/2015	17/04/2015						
6	<u> </u>	Monitoring	2d	16/04/2015	17/04/2015						
7		□ Generacion de Caso de uso de los modulos	25d	20/04/2015	22/05/2015						
8		Configuration Manager	10d	20/04/2015	01/05/2015	4					
9	5	Inventory	5d	04/05/2015	08/05/2015	5					
10	-	Monitoring	10d	11/05/2015	22/05/2015	6					
11		⊡ Diseño del modelo	10d	25/05/2015	05/06/2015	7					
12	-	Creacion del modelo de datos	2d	25/05/2015	26/05/2015						
13		Diseño de la aplicacion	10d	25/05/2015	05/06/2015						
14		⊡Desarrollo	96d	08/06/2015	19/10/2015	2					
15		☐ TMN Integral	96d	08/06/2015	19/10/2015						
16		□ Entregable 1: Inventory	32d	08/06/2015	21/07/2015						
17		⊟Diseño	5d	08/06/2015	12/06/2015						
18		Arquitectura de la base de datos	2d	08/06/2015	09/06/2015						
19		Interfaz Grafica	5d	08/06/2015	12/06/2015						
20		□Desarrollo	27d	15/06/2015	21/07/2015						
21		□ Interfaz Grafica	11d	15/06/2015	29/06/2015	19					
22		Discovery de Equipos de Red	2d	15/06/2015	16/06/2015						
23	<u></u>	Auto-generacion de enlaces	2d	17/06/2015	18/06/2015						
					+			-			


24		Generacion manul de enlaces	2d	19/06/2015	22/06/2015		
25	<u> </u>	Generacion re reportes de vacancia	5d	23/06/2015	29/06/2015		
26		☐ Servicios	10d	30/06/2015	13/07/2015	18	
27	<u> </u>	Discovery de equipos en red	5d	30/06/2015	06/07/2015		
28	<u> </u>	Auto-generación de enlaces	5 d	30/06/2015	06/07/2015		
29	<u> </u>	Generación manual de enlaces	5 d	30/06/2015	06/07/2015		
30	<u> </u>	Generación de Reportes de vacancia	5 d	07/07/2015	13/07/2015		
31		⊟Testing	6d	14/07/2015	21/07/2015	21,26	
32		□ Desarrollo de Casos de Testing	2d	14/07/2015	15/07/2015		
33		Inventory	2d	14/07/2015	15/07/2015		
34		□ Pruebas del Sistema	4d	16/07/2015	21/07/2015	32	
35		Inventory	4d	16/07/2015	21/07/2015		
36		□ Entregable 2: Monitoring - Alarmas	14d	22/07/2015	10/08/2015	16	
37		⊡Diseño	2d	22/07/2015	23/07/2015		
38		Arquitectura de la Base de Datos	1d	22/07/2015	22/07/2015		
39		Interfaz Grafica	2d	22/07/2015	23/07/2015		
40		□Desarrollo	9d	24/07/2015	05/08/2015		
41		□ Interfaz Grafica	4d	24/07/2015	29/07/2015	39	
42		Generacion de Alarmas de interfaz Equipo (2d	24/07/2015	27/07/2015		
43	<u> </u>	Configuración de mails automaticos	2d	28/07/2015	29/07/2015		
44		☐ Servicios	5d	30/07/2015	05/08/2015	38	
45	5	Generacion de Alarmas de Interfaz/Equipo (3d	30/07/2015	03/08/2015		
46	5	Configuracion de mails automaticos	2d	04/08/2015	05/08/2015		
47		⊡Testing	3d	06/08/2015	10/08/2015	40	
48		□ Desarrollo de Casos de Testing	1d	06/08/2015	06/08/2015		

49		Alarmas	1d	06/08/2015	06/08/2015		
50		□ Pruebas de Sistema	2d	07/08/2015	10/08/2015	48	
51		Alarmas	2d	07/08/2015	10/08/2015		
52		☐ Entregable 3: Monitoring - Performance	24d	11/08/2015	11/09/2015	36	
53		⊡Diseño	3d	11/08/2015	13/08/2015		
54		Arquitectura de Base de Datos	1d	11/08/2015	11/08/2015		
55	□	Interfaz Grafica	2d	12/08/2015	13/08/2015		
56		□Desarrollo	15d	14/08/2015	03/09/2015		
57		⊞ Interfaz Grafica	5d	14/08/2015	20/08/2015	55	
63		⊞ Servicios	10d	21/08/2015	03/09/2015	54	
69		□Testing	6d	04/09/2015	11/09/2015	56	
70		□ Desarrollo de Casos de testing	1d	04/09/2015	04/09/2015		
71		Performance	1d	04/09/2015	04/09/2015		
72		□ Pruebas del sistema	5d	07/09/2015	11/09/2015	70	
73		Performance	5d	07/09/2015	11/09/2015		
74		☐ Entregable 4: Configuration Manager	96d	08/06/2015	19/10/2015		
75		⊡Diseño	73d	08/06/2015	16/09/2015		
76		Arquitectura de Base de Datos	1d	08/06/2015	08/06/2015		
77	□	Interfaz Grafica	2d	15/09/2015	16/09/2015		
78		□Desarrollo	14d	17/09/2015	06/10/2015	75	
79		⊞ Interfaz Grafica	4d	17/09/2015	22/09/2015	77	
84		⊞ Servicios	10d	23/09/2015	06/10/2015		
89		⊞Testing	9d	07/10/2015	19/10/2015	78	
94		□Implementacion	19d	20/10/2015	13/11/2015	16,36,52,74	
95		Generacion de un ambiente	5d	20/10/2015	26/10/2015		

96		Presentacion del proyecto	1d	27/10/2015	27/10/2015	95	
97		☐ Pruebas Generales	5d	09/11/2015	13/11/2015	95	
98	□	Pruebas Integrales del Sistema	5d	09/11/2015	13/11/2015		
99		□ Pruebas de los modulos	9d	27/10/2015	06/11/2015	95	
100	<u> </u>	Configuration Manager	2d	27/10/2015	28/10/2015		
101	130	Inventory	2d	29/10/2015	30/10/2015		
102	130	Monitoring - Alarmas	2d	03/11/2015	04/11/2015		
103	130	Monitoring - Performance	2d	05/11/2015	06/11/2015		
104		☐ Gestion y control de cambios	3d?	20/10/2015	22/10/2015	14	
105		□ Revisión y análisis de los cambios propuestos	1d	20/10/2015	20/10/2015		
106		Análisis de impacto	1d	20/10/2015	20/10/2015		
107		Análisis de factibilidad	1d	20/10/2015	20/10/2015		
108		⊟Generación de un plan de cambios	2d?	21/10/2015	22/10/2015	105	
109		Generación de casos de uso para el cambio	2d	21/10/2015	22/10/2015		
110		Implementación del cambio	1d?	21/10/2015	21/10/2015		

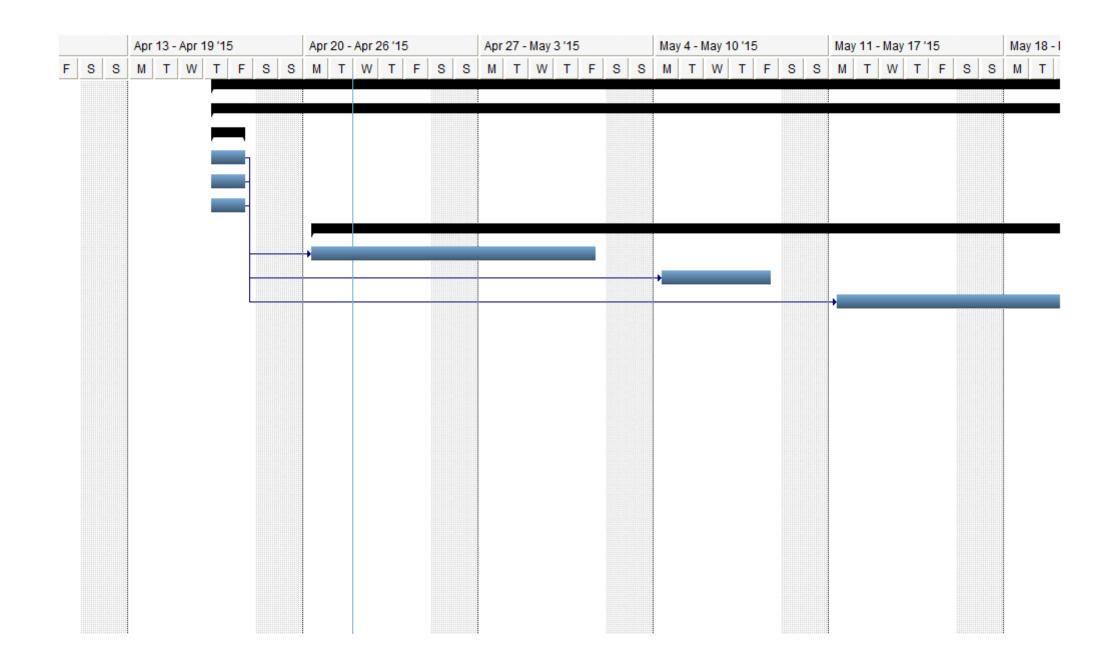

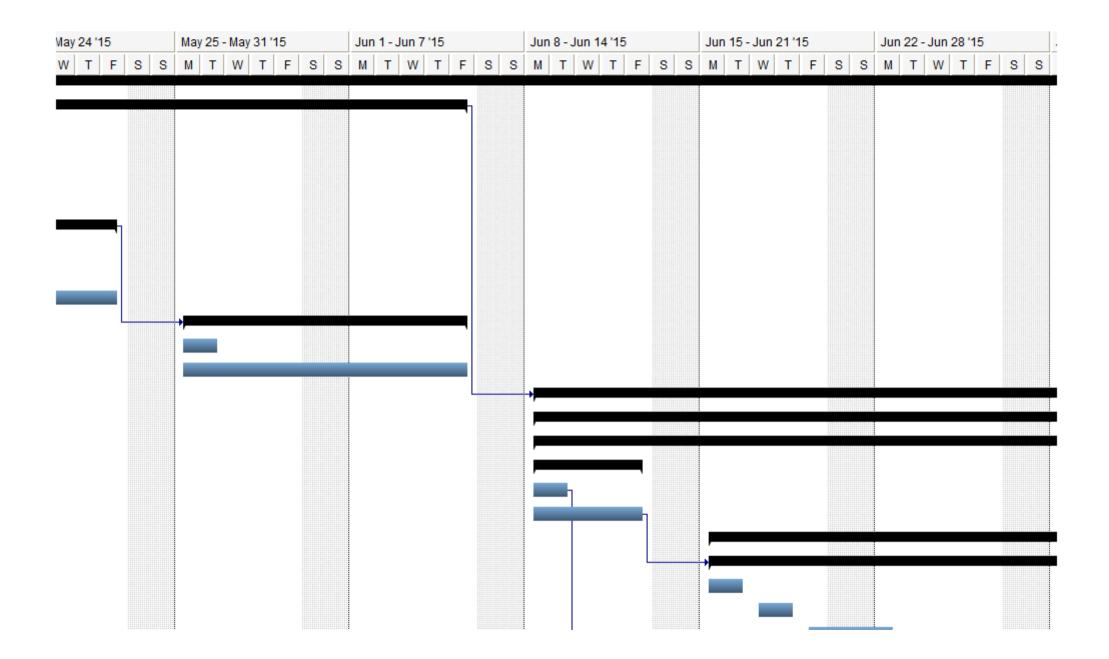


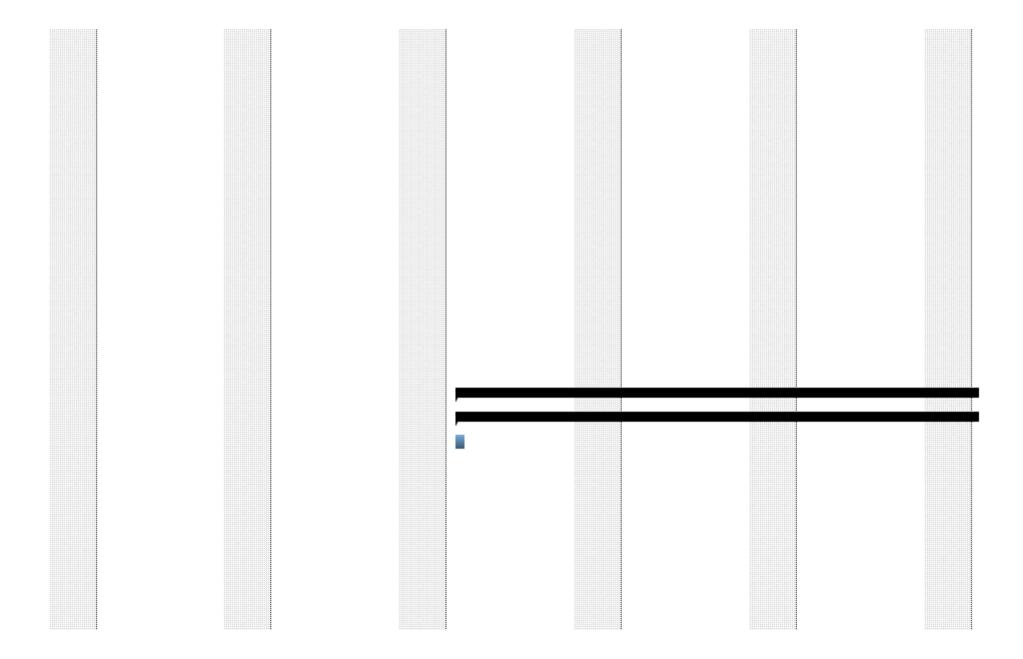

	•		•		
	**************************************	***************************************	**************************************	**************************************	***************************************
			•		
			•		
-1	11011111111111111111111111111111111111		* I	• • • • • • • • • • • • • • • • • • •	
			•	•	
			•		
	**************************************	***************************************	•	**************************************	
			:		
	•		•	•	
::::::::::::::::::::::::::::::::::::::			* I	• • • • • • • • • • • • • • • • • • •	
	• • • • • • • • • • • • • • • • • • •		•	•	
	•	***************************************	•	•	***************************************
	• • • • • • • • • • • • • • • • • • •		•		
	• • • • • • • • • • • • • • • • • • •		• • • • • • • • • • • • • • • • • • •	•	
•	•	•	•	************ *	
					* 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1
	•		•	•	
	***************************************		***************************************	***************************************	
	**************************************	***************************************	**************************************		***************************************
::::::::::::::::::::::::::::::::::::::		***************************************	:		
			•		
			•		
			•		
-1		************ *	• • • • • • • • • • • • • • • • • • •		
- 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1			•		
	•		•	***************************************	***************************************
	• • • • • • • • • • • • • • • • • • •		•	•	
	***************************************		***************************************	***************************************	
	•	•	•	**************************************	
	• • • • • • • • • • • • • • • • • • •		• • • • • • • • • • • • • • • • • • •	•	
*10000000000000000000000000000000000000					* 100 H
	***************************************			***************************************	***************************************
	[[] [] [] [] [] [] [] [] [] [10000000000000000000000000000000000000


					•
100000000000000000000000000000000000000	• • • • • • • • • • • • • • • • • • •				
: C C C C C C C C C	:				
	•				•
***************************************	•				***************************************
	•	•		**************************************	
	• • • • • • • • • • • • • • • • • • • •			***************************************	
*10000000000000000000000000000000000000	•				* 100 100 100 100 100 100 100 100 100 10


Jun 29 - Jul 5 '15	Jul 6 - Jul 12 '15		Jul 13 -	Jul 19	9 '15			Jul 2	20 - J	ul 26	15		Jul	27 - /	Aug 2	'15			Aug	g 3 - /	Aug 9	'15	
M T W T F S S	M T W T F	s s	М	W	Т	F	SS	М	Т	w	T F	S S	М	Т	W	Т	F S	S	М	Т	W	Т	F
									-														
									_														
•																							

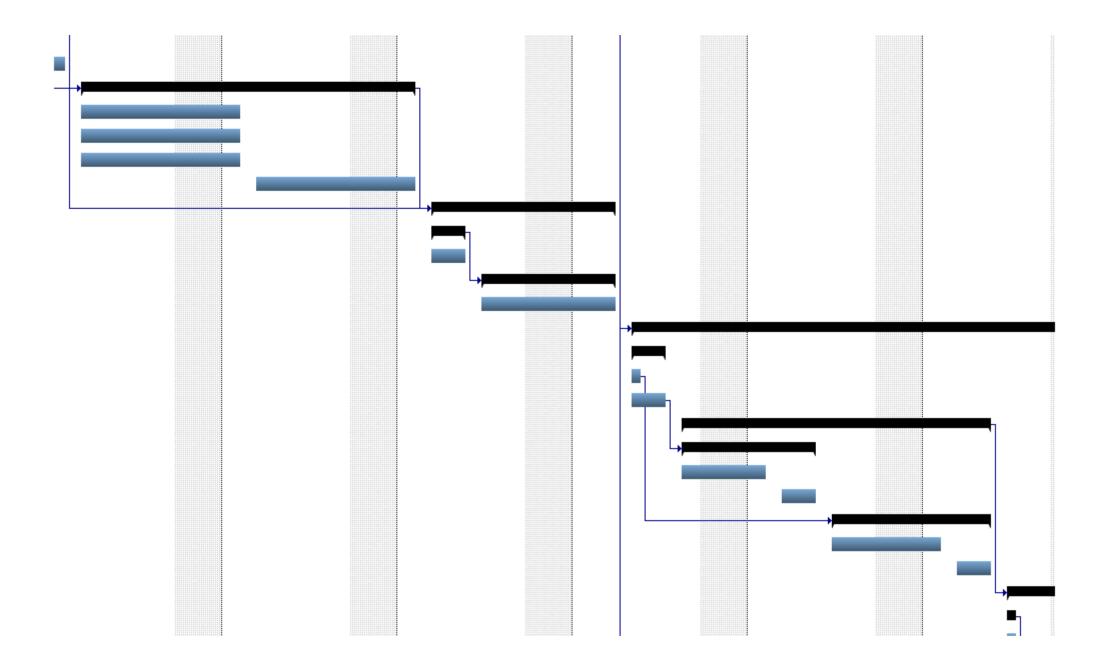

•••••••••••••••••••••••••••••••••••••••	•	•	•		
	40000000000000000000000000000000000000				

	Aug 10 - Aug 16 '15								Aug 17 - Aug 23 '15							Aug 24 - Aug 30 '15						Aug 31 - Sep 6 '15						Sep 7 - Sep 13 '15							Sep 14 - Sep 2				
s s					F	5	8 8					Т		S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S			W

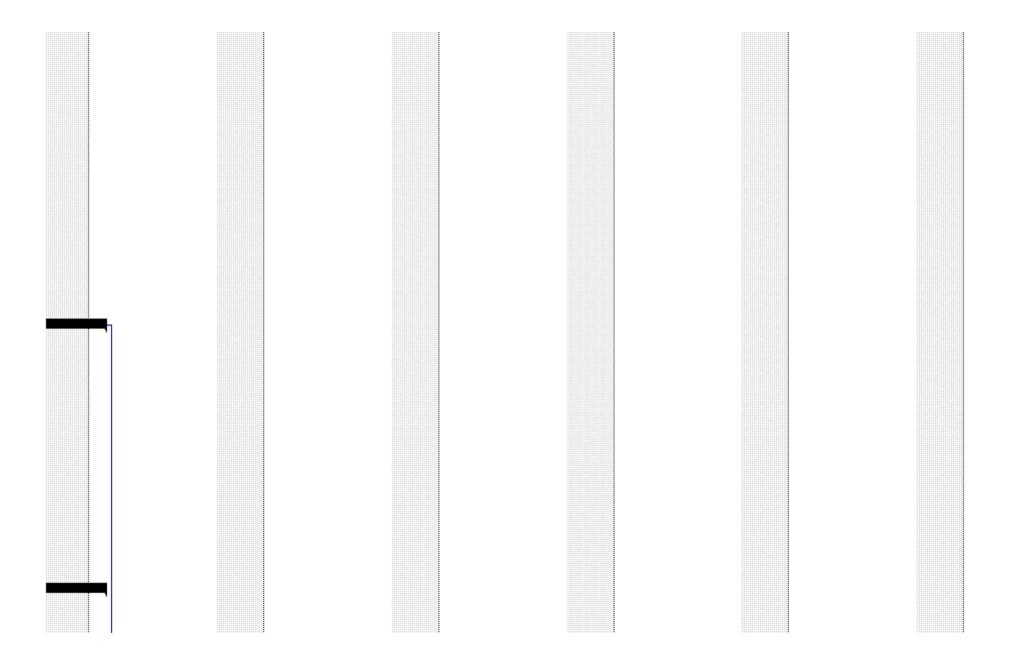


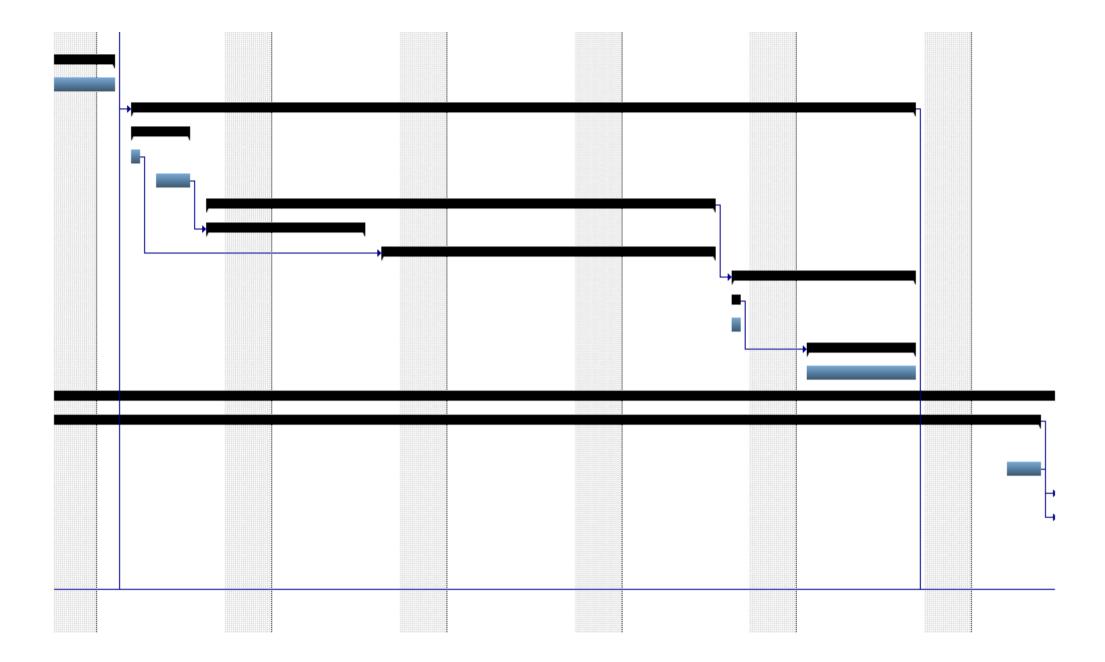


::::::::::::::::::::::::::::::::::::::	: 10:000 10:00 10:00 10:00 10:00 10:00 10:00 10:00 10:00 10:00 10:00 10:00 10:00 10:00 10:00 10:00 10:00 10:00	: I I I I I I I I I I I I I I I I I I I		:	
	•				
::::::::::::::::::::::::::::::::::::::	::::::::::::::::::::::::::::::::::::::	10000000000000000000000000000000000000	::::::::::::::::::::::::::::::::::::::	11011111111111111111111111111111111111	
	-100-100-100-100-100-100-100-100-100-10	• • • • • • • • • • • • • • • • • • •	-10-41-10-10-10-10-10-10-10-10-10-10-10-10-10	• • • • • • • • • • • • • • • • • • •	
			-10-10-10-10-10-10-10-10-10-10-10-10-10-		
•	•	•	- D-11111- D-11111- D-1111- B		
•	•	•	•	•	
::::::::::::::::::::::::::::::::::::::	: 1000001110111111111111111111111111111	: I : : : : : : : : : : : : : : : : : :	::::::::::::::::::::::::::::::::::::::	:	100010011111000
01111-10-01-10111	*1011111111111111111111111111111111111	-1001111111111111111111111111111111111	-101111-101-101-10111 :	-1001111111111111111111111111111111111	*15011111110170011101111 *
			**************************************		*100***********************************
		:		::::::::::::::::::::::::::::::::::::::	
•	•	•			
	1000010000100001	::::::::::::::::::::::::::::::::::::::		::::::::::::::::::::::::::::::::::::::	::::::::::::::::::::::::::::::::::::::
•	•	•	::::::::::::::::::::::::::::::::::::::	:	
11.001.101.101.101.101.101.101.101.101.	: I : I : I : I : I : I : I : I : I : I	::::::::::::::::::::::::::::::::::::::	::::::::::::::::::::::::::::::::::::::	: 100 m 1 m 1 m 1 m 1 m 1 m 1 m 1 m 1 m 1	
0.111111010101010111	-CO-1411-1-0-CO-1-CO-141-		-00-111-10-00-00-10-111-		
10000000000000000000000000000000000000					
		-1111111111111111111111111111111111111	10300110311111131111 1	-1111111111111111111111111111111111111	
			**************************************		*1*************************************
		:		::::::::::::::::::::::::::::::::::::::	
•	•	•			
	1000010000100001	::::::::::::::::::::::::::::::::::::::		:10:001:10:10:10:10:10:10:10:10:10:10:10	::::::::::::::::::::::::::::::::::::::
•	•	•	-10:11:1:10:11:10:11:1	:	
11111111111111111111111111111111111111	: I : : : : : : : : : : : : : : : : : :	: I		::::::::::::::::::::::::::::::::::::::	
	-10111111111111111111111111111111111111			31011111111111111111111111111111111111	
		10.00.00.00.00.00.00		:::::::::::::::::::::::::::::::::::::::	
::::::::::::::::::::::::::::::::::::::					
::::::::::::::::::::::::::::::::::::::	::::::::::::::::::::::::::::::::::::::	::::::::::::::::::::::::::::::::::::::	::::::::::::::::::::::::::::::::::::::	31011111111111111111111111111111111111	
		- 100 H	- - - - - - - - - -	- 100 H	
***************************************		***************************************		***************************************	
::::::::::::::::::::::::::::::::::::::		- 100 110 110 110 110 110 110 110 110 11	- - - - - - - - - -	*	
•	•	•			
11111111111111111111111111111111111111	- 14-14-14-14-14-14-14-14-14-14-14-14-14-1		::::::::::::::::::::::::::::::::::::::		
0.001-0.00101-0.0000		00000000000000000000000000000000000000	500000 50000 50000 E	00000000000000000000000000000000000000	110111111111111111111111111111111111111
	• • • • • • • • • • • • • • • • • • •	• • • • • • • • • • • • • • • • • • •	•		
			-10-10-10-10-10-10-10-10-10-10-10-10-10-		
	- - - - - - - - - -			-1	
•	•	•	•	•	
::::::::::::::::::::::::::::::::::::::	: 10:0001110111111111111111111111111111	: I : : : : : : : : : : : : : : : : : :	110001100111110011	:::::::::::::::::::::::::::::::::::::::	
::::::::::::::::::::::::::::::::::::::			31011111111111111111111111111111111111		
11111111111111111111111111111111111111	- 14-14-14-14-14-14-14-14-14-14-14-14-14-1				
011111111111111111111111111111111111111	-10-111-10-111-10-111-1	00001000000000000000000000000000000000	50000000000000000000000000000000000000	::::::::::::::::::::::::::::::::::::::	110111111111111111111111111111111111111
	• • • • • • • • • • • • • • • • • • •	• • • • • • • • • • • • • • • • • • •	• • • • • • • • • • • • • • • • • • •	• • • • • • • • • • • • • • • • • • •	
			- politic politic politic		
	- 10.000 to 10.0	- - - - - - - - - -			
•	•	•			
	: ICC. ICC. ICC. ICC. ICC. ICC. ICC. ICC	: I : : : : : : : : : : : : : : : : : :	100000000000000000000000000000000000000	: I : : : : : : : : : : : : : : : : : :	101111101111111111
	•				
0.001.00.001.0000.	::::::::::::::::::::::::::::::::::::::	::::::::::::::::::::::::::::::::::::::	111111111111111111111111111111111111111	::::::::::::::::::::::::::::::::::::::	
•	•	•	•	•	
		::::::::::::::::::::::::::::::::::::::		::::::::::::::::::::::::::::::::::::::	
	- 10-1111 11-1111 11-1111 11-1111 11-1111 11-1111 11-11111 11-11111 11-11111 11-11111 11-11111 11-11111 11-11111 11-11111 11-11111 11-11111 11-11111 11-1111111 11-111111 11-1111111 11-111111 11-111111 11-11111111	- 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1		- 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1	
::::::::::::::::::::::::::::::::::::::	-14414-4444-4444-4444-4444-4444-4444-4444-4444	-1001110110110111111111111111111111111		-1001111111111111111111111111111111111	
01111101111111111 1		-10-11-10-11-10-11-10-11-1			
::::::::::::::::::::::::::::::::::::::	-1441 H - 1441 H - 14	-14-14-14-14-14-14-14-14-14-14-14-14-14-			-110-1111 110-1111 110-111 1
•			•		
30000000000000000000000000000000000000		**************************************			
***************************************		***************************************	::::::::::::::::::::::::::::::::::::::	***************************************	
***************************************		***************************************		***************************************	
::::::::::::::::::::::::::::::::::::::		: I I I I I I I I I I I I I I I I I I I	::::::::::::::::::::::::::::::::::::::	::::::::::::::::::::::::::::::::::::::	
::::::::::::::::::::::::::::::::::::::		::::::::::::::::::::::::::::::::::::::	::::::::::::::::::::::::::::::::::::::	***********************	
::::::::::::::::::::::::::::::::::::::	:10:11:10:11:10:11:10:11:	:10:11:10:10:10:10:10:10:10:10:10:10:10:	:10:00:10:00:10:00:1	:10:11:10:10:10:10:10:10:10:10:10:10:10:	
0.001.00.001.00.001	naminaminaliii	naminaminiiii		naminaminiiii	100000000000000000000000000000000000000
201011-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1		-1000000000000000000000000000000000000	-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1		
		1000 H			

***************************************		***************************************		***************************************	
::::::::::::::::::::::::::::::::::::::		:	: ::::::::::::::::::::::::::::::::::::	:::::::::::::::::::::::::::::::::::::::	
201120112011 2	18111111111111111111111111111111111111	1000100001000	::::::::::::::::::::::::::::::::::::::	100010000000	
::		:			
emineminem:	:18:00:10:00:11:18:00:	:18:001:001111:18:00	:10:001:10:001:10:00	:10001100111110001	:1:::::::::::::::::::::::::::::::::::::
::::::::::::::::::::::::::::::::::::::	-1011111111111111111111111111111111111	::::::::::::::::::::::::::::::::::::::	::::::::::::::::::::::::::::::::::::::	::::::::::::::::::::::::::::::::::::::	
01111-10100101111		1011111000010111	101111000010111		
::::::::::::::::::::::::::::::::::::::					
0.001.00.001.00.001	naminaminaliii	naminaminiiii		naminaminiiii	100000000000000000000000000000000000000

20 '15		Sep	21 - S	ep 27	7 '15			Sep 28 - Oct 4 '15						Oct 5 - Oct 11 '15						Oct 12 - Oct 18 '15					Oct 19 - Oct 25 '15							Oct 2				
T F S	S	М	TV	V T	F	S	S	М	Т	W	T	F	S	S	М	Т	W	Т	F	S	S	М	T	W	Т	F	S	S	М	Т	W	Т	F	S	S	M
																													_							

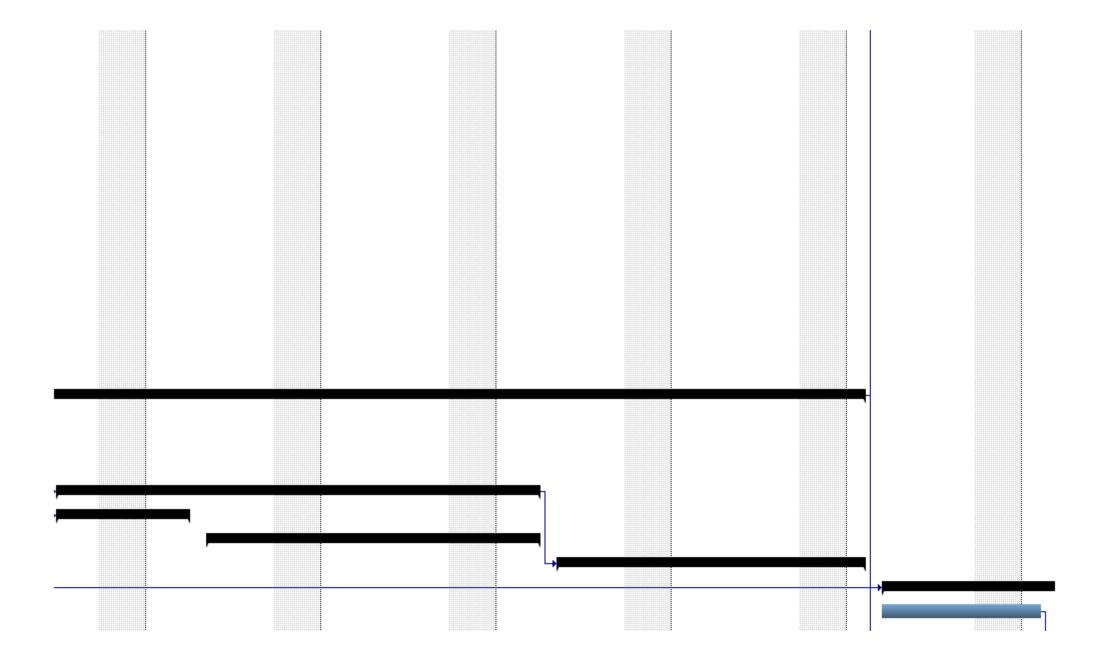

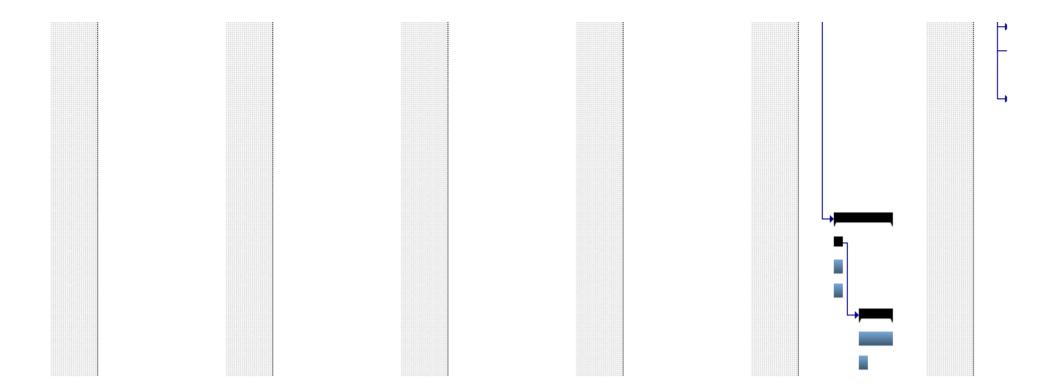

o - Nov	15		Nov 2 - Nov 8 '15								Nov 9 - Nov 15 '15							Nov 16 - Nov 22 '15							
T W	Т	F	S	s	М	Т	W	Т	F	S	s	М	Т	W	Т	F	S	s	М	Т	W	Т	F	s	5

